


ID	Task Mode	Task Name	Duration	Start	Finish	3	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
						H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
1		BAFS High Level Programme	67.18 mons	Thu 21/12/23	Mon 20/08/29															
2		OBC	10.36 mons	Thu 21/12/23	Mon 04/11/24															
3		OBC Initial Compilation	0 days	Thu 21/12/23	Thu 21/12/23															
4		OBC Final Compilation	0 days	Fri 12/01/24	Fri 12/01/24															
5		BCC January Cabinet Endorsement of OBC	0 days	Wed 31/01/24	Wed 31/01/24															
6		BCC Issue of OBC to EA LPRG	0 days	Thu 01/02/24	Thu 01/02/24															
7		Resolution of Comments with BCC and LPRG	2 mons	Thu 01/02/24	Tue 02/04/24															
8		<i>Time Risk Allowance</i>	1 mon	Wed 03/04/24	Thu 02/05/24															
9		OBC Approval - BCC, recommendation for endorsement - EA LPRG	0 days	Thu 02/05/24	Thu 02/05/24															
10		Defra and HMT Approval Period	6 mons	Fri 03/05/24	Mon 04/11/24															
11		Defra and HMT Approval (TBC - election Autumn 2024?)	0 mons	Mon 04/11/24	Mon 04/11/24															
12		Key Dates	52.5 mons	Tue 14/01/25	Tue 19/06/29															
13		Commence FBC	0 mons	Tue 14/01/25	Tue 14/01/25															
14		Design Freeze for EIA Scoping	0 mons	Fri 01/08/25	Fri 01/08/25															
15		Design Freeze for ES & Planning (preparation of both)	0 mons	Fri 20/03/26	Fri 20/03/26															
16		Submit for TWAO	0 mons	Fri 09/04/27	Fri 09/04/27															
17		Obtain TWAO Consent	0 mons	Wed 14/06/28	Wed 14/06/28															
18		Finalisation of FBC - Final Assurance Decision	0 mons	Tue 19/06/29	Tue 19/06/29															
19		FBC Summary	63.82 mons	Thu 01/02/24	Tue 19/06/29															
20		Engagement planning	2 mons	Thu 01/02/24	Tue 02/04/24															
21		Preparation for procurement by BCC	5 mons	Mon 12/02/24	Fri 12/07/24															
22		Engagement - awareness raising and constraints/opportunities	3 mons	Mon 30/09/24	Mon 30/12/24															
23		Procurement for FBC Consultant(s)	6 mons	Mon 15/07/24	Tue 14/01/25															
24		Finalisation of FBC including HMT, Defra and LPRG assurance	12 mons	Thu 15/06/28	Tue 19/06/29															
25		FBC1 - Entire Scheme [Main Consultant] with carve outs for FBC2 and FBC3 - Design	28 mons	Wed 15/01/25	Wed 26/05/27															
26		General FBC Activities inc Design Development in tandem with surveys	6.5 mons	Wed 15/01/25	Fri 01/08/25															
27		Site Surveys	6 mons	Wed 15/01/25	Thu 17/07/25															
28		General FBC Activities inc Design Development dependent on surveys, public engagement	14 mons	Wed 15/01/25	Fri 20/03/26															
29		Design Freeze for EIA Scoping	0 mons	Fri 01/08/25	Fri 01/08/25															
30		End of stage comments (informal gateway)	2 mons	Mon 23/03/26	Thu 21/05/26															
31		Detailed Design finalisation for Construction Information / for Tender	12 mons	Fri 22/05/26	Wed 26/05/27															
32		Western Harbour Reach	22 mons	Mon 31/03/25	Thu 04/02/27															
33		Masterplan Concept - RIBA 2 - available (by others)	0 mons	Mon 31/03/25	Mon 31/03/25															
34		Design Development to enable freeze for EIA Scoping	4 mons	Mon 31/03/25	Wed 30/07/25															
35		Site Surveys	6 mons	Thu 31/07/25	Fri 30/01/26															
36		Further Development / Detailed Design for Construction Information	12 mons	Mon 02/02/26	Thu 04/02/27															
37		St Philips Marsh Reach	22 mons	Mon 31/03/25	Thu 04/02/27															
38		Masterplan Concept - RIBA 2 - available (by others)	0 mons	Mon 31/03/25	Mon 31/03/25															
39		Design Development to enable freeze for EIA Scoping	4 mons	Mon 31/03/25	Wed 30/07/25															
40		Site Surveys	6 mons	Thu 31/07/25	Fri 30/01/26															
41		Further Development / Detailed Design for Construction Information	12 mons	Mon 02/02/26	Thu 04/02/27															
42		Ecological Survey	15 mons	Wed 15/01/25	Tue 21/04/26															
43		Confirmation of Surveys Required (Ecology)	1 mon	Wed 15/01/25	Thu 13/02/25															
44		Procurement for Ecology Surveys	2 mons	Fri 14/02/25	Wed 16/04/25															
45		Undertake Surveys (Ecology)	12 mons	Thu 17/04/25	Tue 21/04/26															

Project: BAFS forward program
Date: Tue 16/01/24

Task		Project Summary		Manual Task		Start-only		Deadline		Manual Progress	
Split		Inactive Task		Duration-only		Finish-only		Critical		Critical Split	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Critical Milestone		Progress	
Summary		Inactive Summary		Manual Summary		External Milestone		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	
						H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
46		Potential for updating surveys (when completed greater than 18months before Consent submitted)	0 mons	Tue 21/04/26	Tue 21/04/26															
47		Consenting (under TWAO) - inc ES	34 mons	Fri 01/08/25	Wed 14/06/28															
48		Preparation and Submission	32 mons	Fri 01/08/25	Thu 13/04/28															
49		Commencement	0 mons	Fri 01/08/25	Fri 01/08/25															
50		Finalisation of EIA Scoping	3 mons	Mon 04/08/25	Mon 03/11/25															
51		Scoping Opinion (by SoS)	2 mons	Tue 04/11/25	Fri 02/01/26															
52		Environmental Statement Preparation	12 mons	Mon 05/01/26	Thu 07/01/27															
53		Public Consultation 1	2 mons	Wed 08/07/26	Mon 07/09/26															
54		Public Consultation 2	2 mons	Fri 08/01/27	Wed 10/03/27															
55		Engagement and Application overarching processes	32 mons	Mon 04/08/25	Thu 13/04/28															
56		Finalisation of Application and Supporting Information	9 mons	Wed 08/07/26	Fri 09/04/27															
57		Submission to Planning Inspectorate	0 mons	Fri 09/04/27	Fri 09/04/27															
58		Consenting Process by SoS	14 mons	Mon 12/04/27	Wed 14/06/28															
59		Pre-enquiry	6 mons	Mon 12/04/27	Tue 12/10/27															
60		Public Enquiry	4 mons	Wed 13/10/27	Fri 11/02/28															
61		Inspector's Report	2 mons	Mon 14/02/28	Thu 13/04/28															
62		SoS Decision	1 mon	Fri 14/04/28	Mon 15/05/28															
63		Judicial Review (JR)	1 mon	Tue 16/05/28	Wed 14/06/28															
64		TWAO Consent Milestone	0 mons	Wed 14/06/28	Wed 14/06/28															
65		Other Consents (to be developed - will run in tandem not in series with TWAO)	6 mons	Wed 26/05/27	Fri 26/11/27															
66		Sufficient design information to prepare and submit other consents	0 mons	Wed 26/05/27	Wed 26/05/27															
67		Other Consents - Listed Building Consent	6 mons	Thu 27/05/27	Fri 26/11/27															
68		Other Consents - EA Permits	6 mons	Thu 27/05/27	Fri 26/11/27															
69		Other Consents - MMO	6 mons	Thu 27/05/27	Fri 26/11/27															
70		Other Consents - Highways Authority	6 mons	Thu 27/05/27	Fri 26/11/27															
71		All necessary consents in place to enable Construction Commencement (full TWAO)	0 mons	Wed 14/06/28	Wed 14/06/28															
72		Works Contracts dependent on full TWAO	22 mons	Wed 13/10/27	Mon 20/08/29															
73		Procurement Preparation	6 mons	Wed 13/10/27	Thu 13/04/28															
74		Tender process	8 mons	Fri 14/04/28	Fri 15/12/28															
75		Obtain Contract costs for FBC	0 mons	Fri 15/12/28	Fri 15/12/28															
76		Contract Award	0 mons	Tue 19/06/29	Tue 19/06/29															
77		Mobilisation	2 mons	Wed 20/06/29	Mon 20/08/29															
78		Possible Works Start (earliest)	0 mons	Tue 19/06/29	Tue 19/06/29															
79		Construction	84 mons	Wed 20/06/29	Fri 18/07/36															
80		Entrance Lock and Netham Lock	18 mons	Wed 20/06/29	Wed 25/12/30															
81		Western Harbour	12 mons	Wed 12/07/34	Mon 16/07/35															
82		Cumberland Road	24 mons	Thu 26/12/30	Mon 03/01/33															
83		City Centre	18 mons	Tue 04/01/33	Tue 11/07/34															
84		Pill, Shirehampton, Sea Mills	18 mons	Wed 31/12/31	Wed 06/07/33															
85		St Anne's	24 mons	Thu 26/12/30	Mon 03/01/33															
86		Upstream	18 mons	Wed 20/06/29	Wed 25/12/30															
87		Bower Ashton	12 mons	Tue 04/01/33	Fri 06/01/34															
88		Feeder and St Philip's	24 mons	Wed 12/07/34	Fri 18/07/36															
89		Construction Completion	0 mons	Fri 18/07/36	Fri 18/07/36															

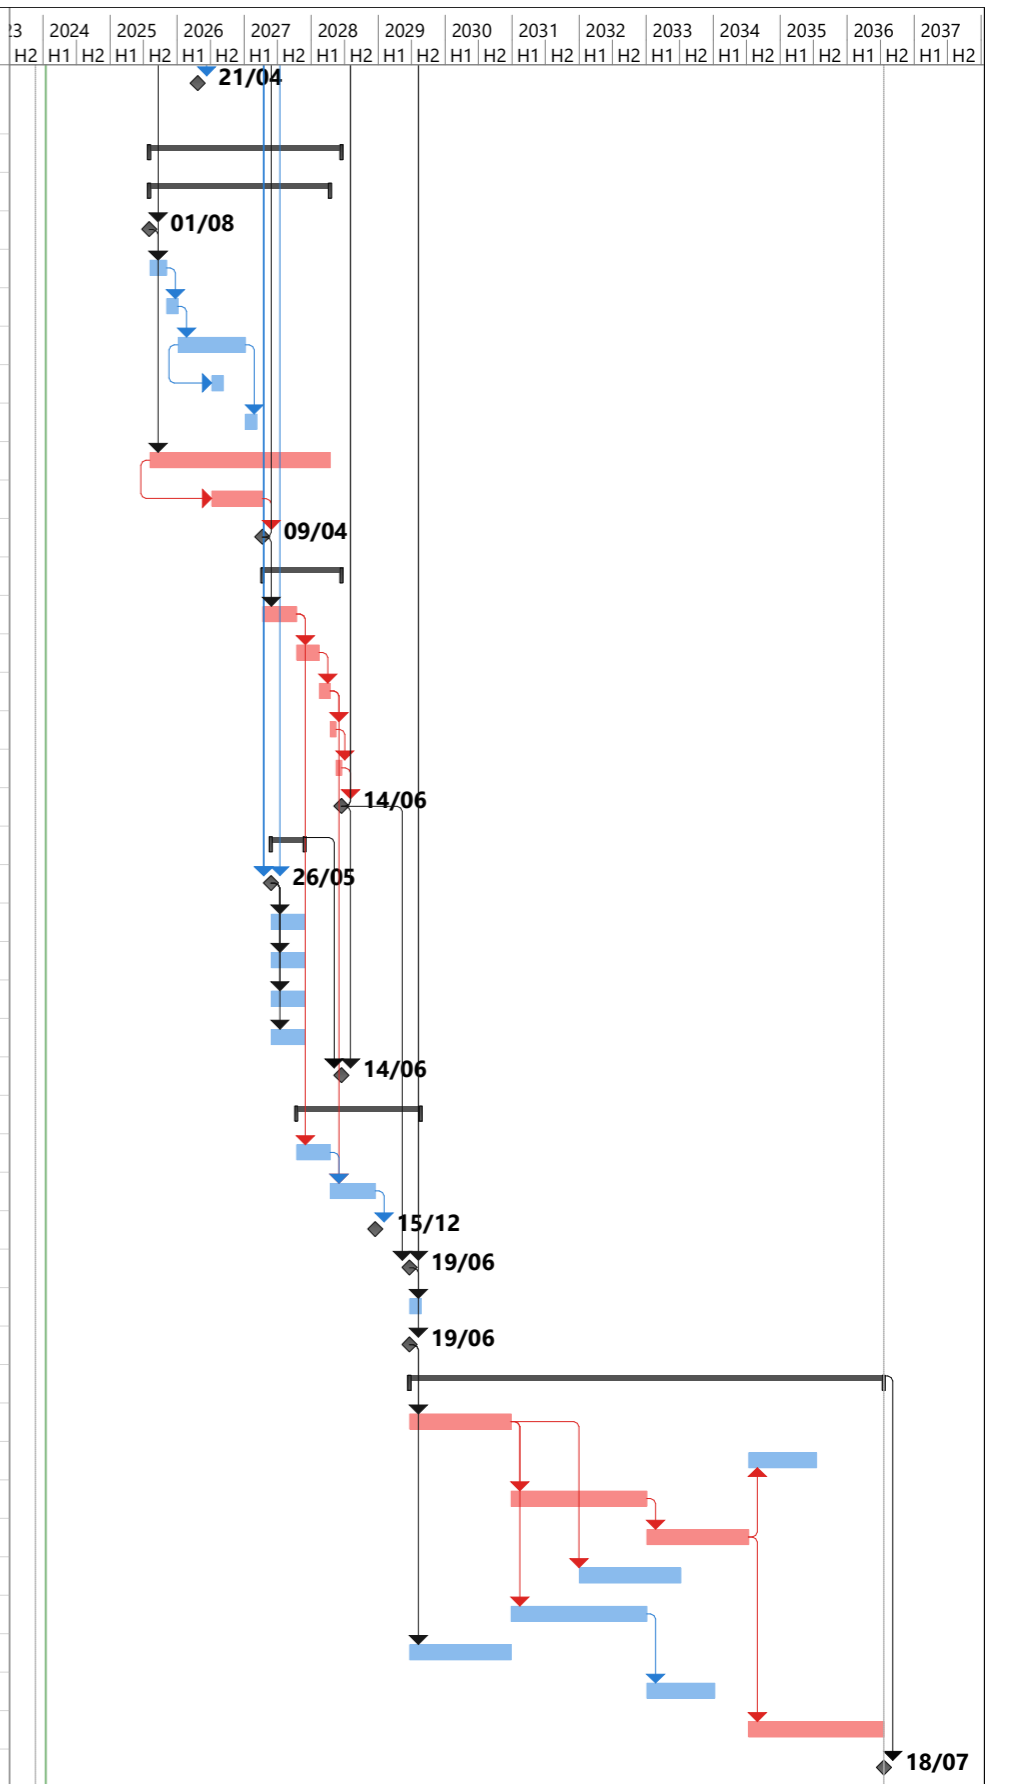

Project: BAFS forward program
Date: Tue 16/01/24

Task		Project Summary		Manual Task		Start-only		Deadline		Manual Progress	
Split		Inactive Task		Duration-only		Finish-only		Critical		Critical Split	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Critical Split		Progress	
Summary		Inactive Summary		Manual Summary		External Milestone		Progress			
